
Voditelj projekta: Ivan Knezić

Datum: Sun 21.6.20



Name	Start	Finish	% Complete	Baseline Start	Baseline Finish
Knjižnica	Mon 1.6.20	Wed 2.9.20	67%	Mon 1.6.20	Mon 31.8.20
Actual Cost	Remaining Cost		Cost	Baseline Cost	
171.024,88 kn	64.067,00 kn		235.091,88 kn	237.286,50 kn	
EAC	ACWP		BCWP	BCWS	
242.839,29 kn	160.122,38 kn		172.461,01 kn	163.831,00 kn	
CV	SV		СРІ	SPI	
12.338,62 kn	-7.370,00 kn		0,98	0,96	

Voditelj projekta: Ivan Knezić Datum: Sun 21.6.20

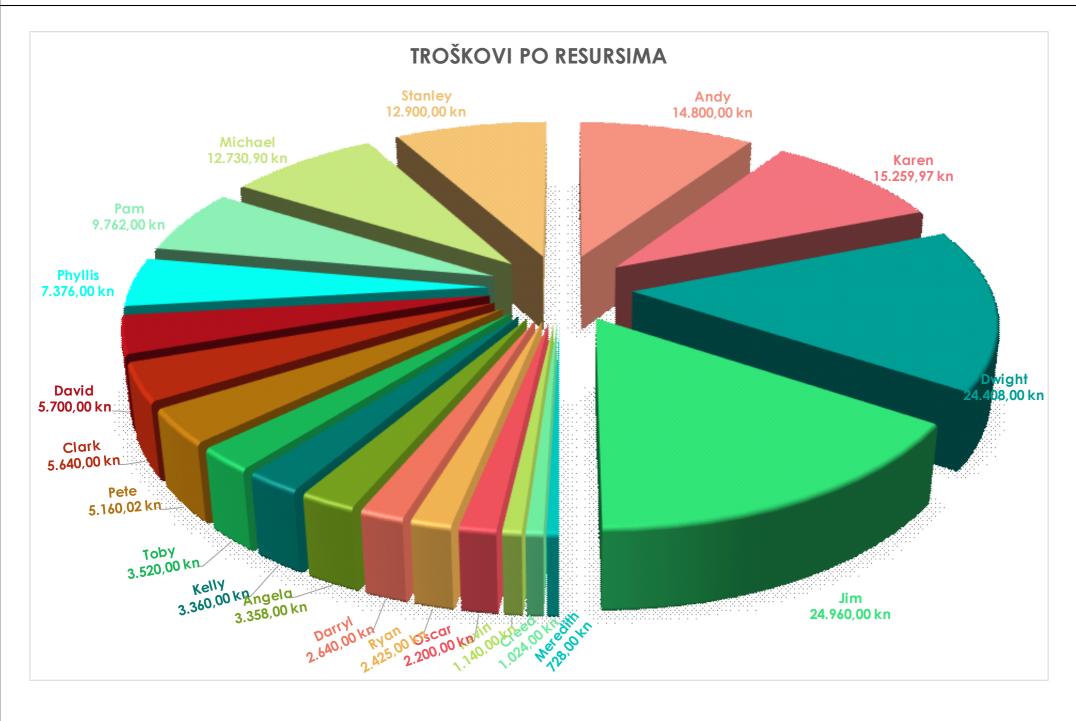

Voditelj projekta: Ivan Knezić

